

# Stakeholder Forum

## Campbeltown Runway 11/29 Project

Date : 16<sup>th</sup> September 2021

Presented by John Lamont



# Agenda

2.00pm – Introduction

2.05pm - Runway closure and operational dates


2.10pm - Project works that will be executed and brought into operation

2.30pm - Access routes

2.35pm - Next steps

2.40pm – Open Discussion

# 1. Runway closure and Operational dates

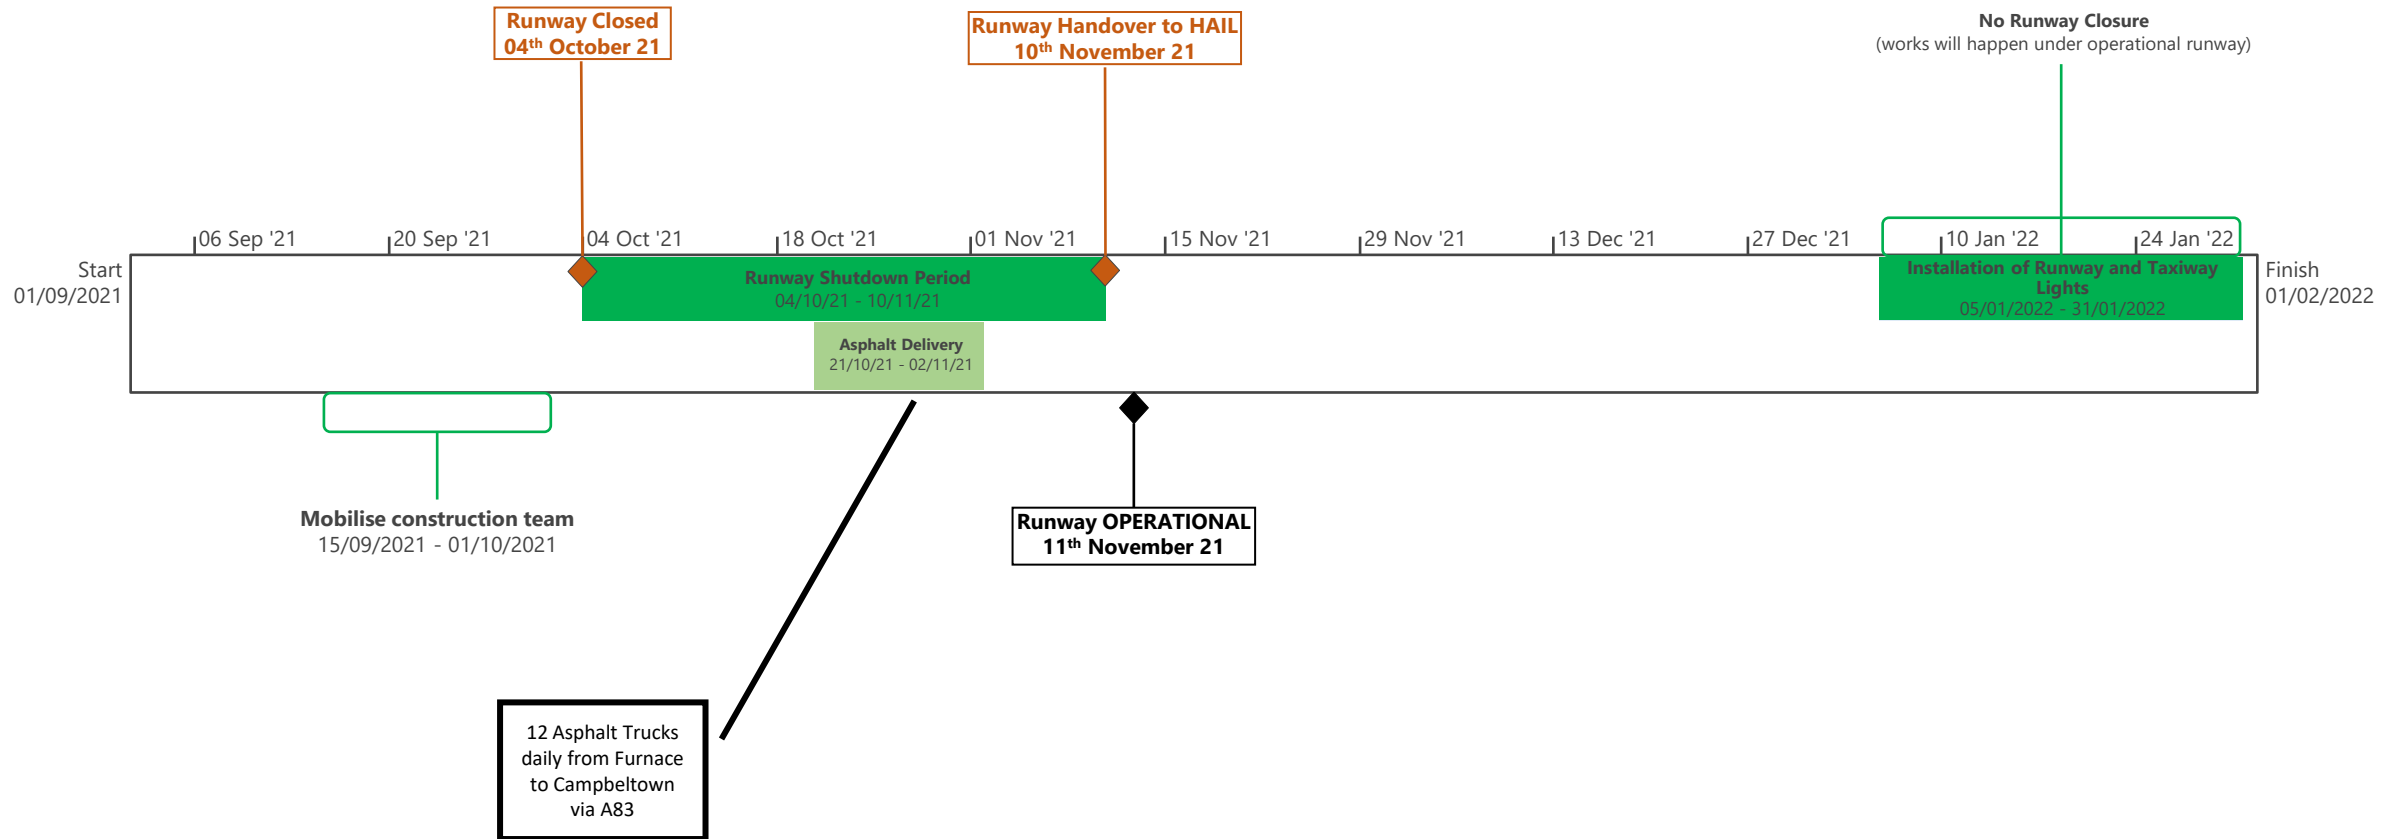

# 2. The Project Works

## 1 Contractor Mobilises 15<sup>th</sup> Sep – 01<sup>st</sup> Oct

1. Mobilise construction team
2. Procurement
3. Setup of compound



## 2. Construction Works 04<sup>th</sup> Oct – 09<sup>th</sup> Nov

1. Removal of 100mm asphalt
2. Apply asphalt reinforcement
3. Apply 100mm new asphalt to finished level




## 3. AGL and Markings 27<sup>th</sup> October 2021 - 09<sup>th</sup> November 2021

Due to extensive lead time for delivery of AGL equipment:


1. The runway will operate with the existing runway edge lights.
2. The existing APAPI's will be relocated to the reduced runway.
3. The Contractor will fit temporary blue lights on the reclassified taxiway.
4. Calibration test to be completed of APAPI's units.
5. Installation of taxiway signage.
6. Runway markings
7. Update of AIP and NOTAM for temporary blue lights.

# 2. The Project Works

## 1. AGL layout on the 11<sup>th</sup> November – RWY 29 in use

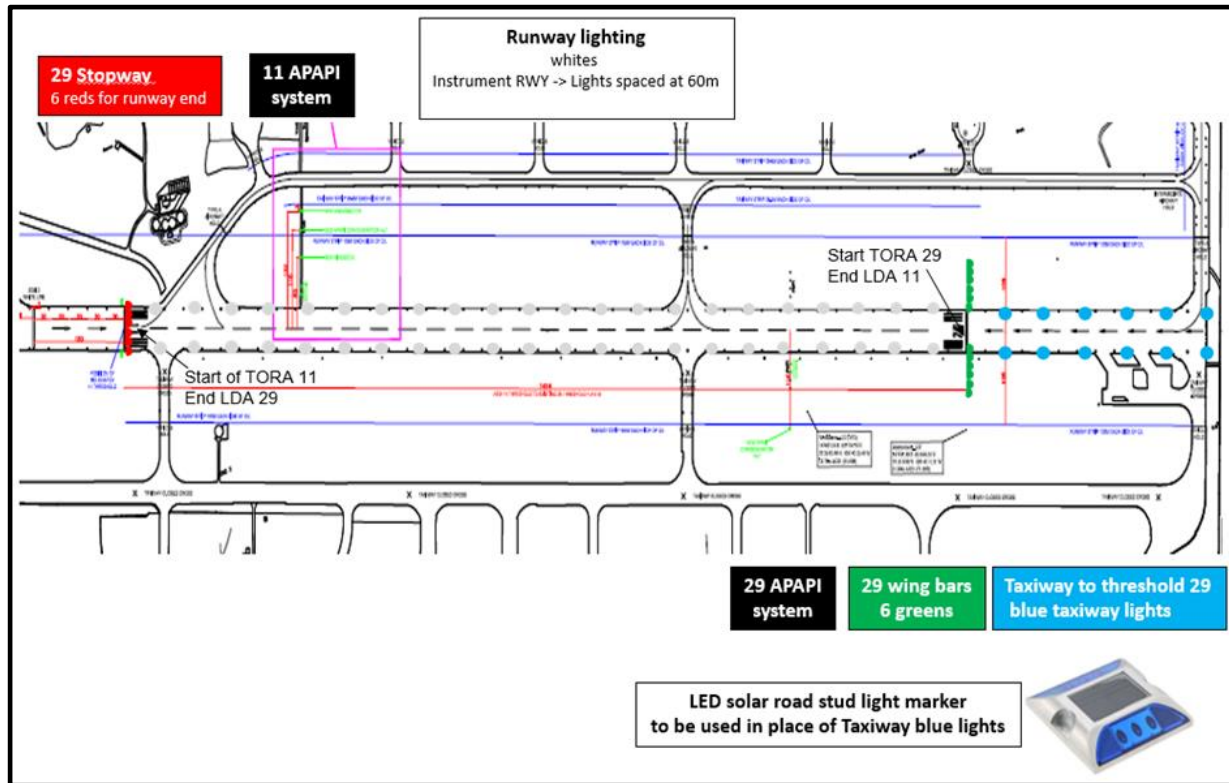

## 2. AGL layout on the 11<sup>th</sup> November – RWY 11 in use

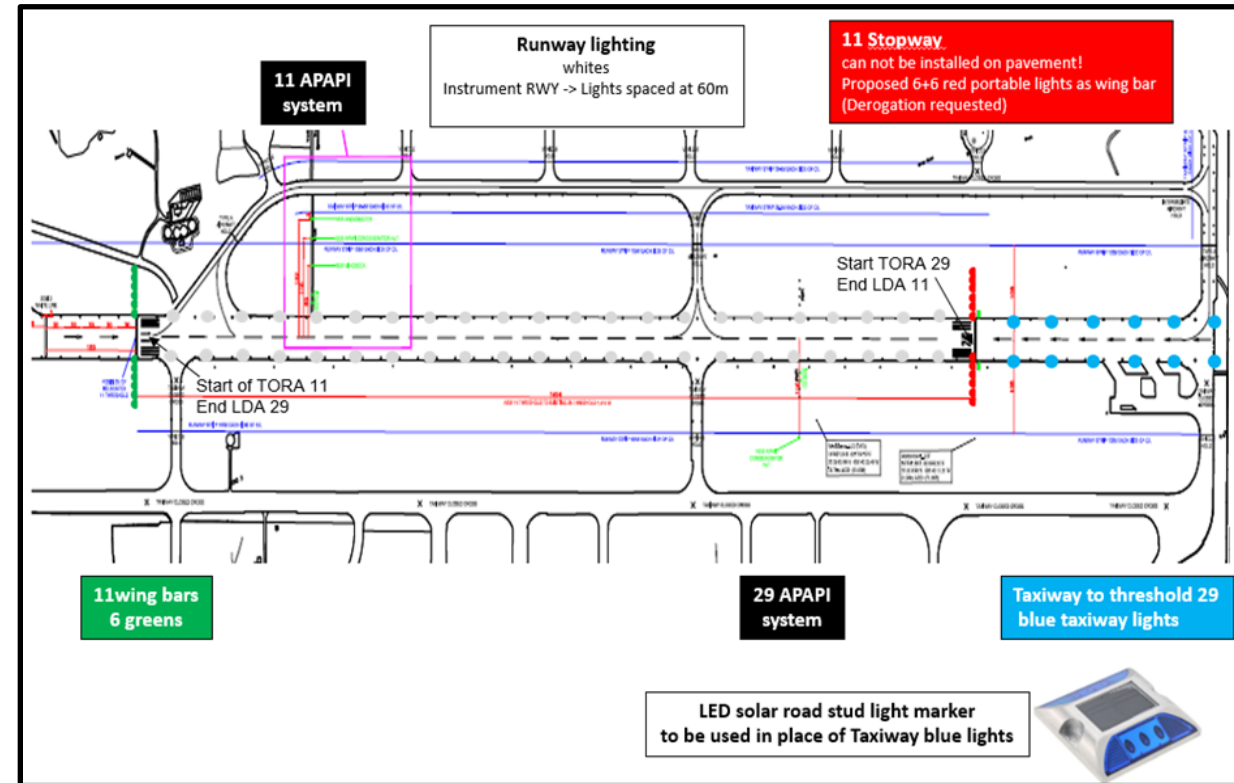

## 2. The Projects Works

### 4. Handover /CAA Approval 10<sup>th</sup> November 2021

1. Handover of Runway from Contractor to HIAL.
2. CAA inspection



### 5. Runway Operational 11<sup>th</sup> November 2021

1. Loganair to resume flights.
2. Air medical services to resume.



### 6. Final installation of AGL 05<sup>th</sup> Jan 2022 – 31<sup>st</sup> Jan 2022


1. Installation of runway edge lights
2. Removal of temporary blue lights
3. Installation of permanent taxiway blue lights

No Runway Closure

# 3. Access Routes

## A83 Truck Road



1. 62 miles on A83
2. A83 under jurisdiction of Transport Scotland

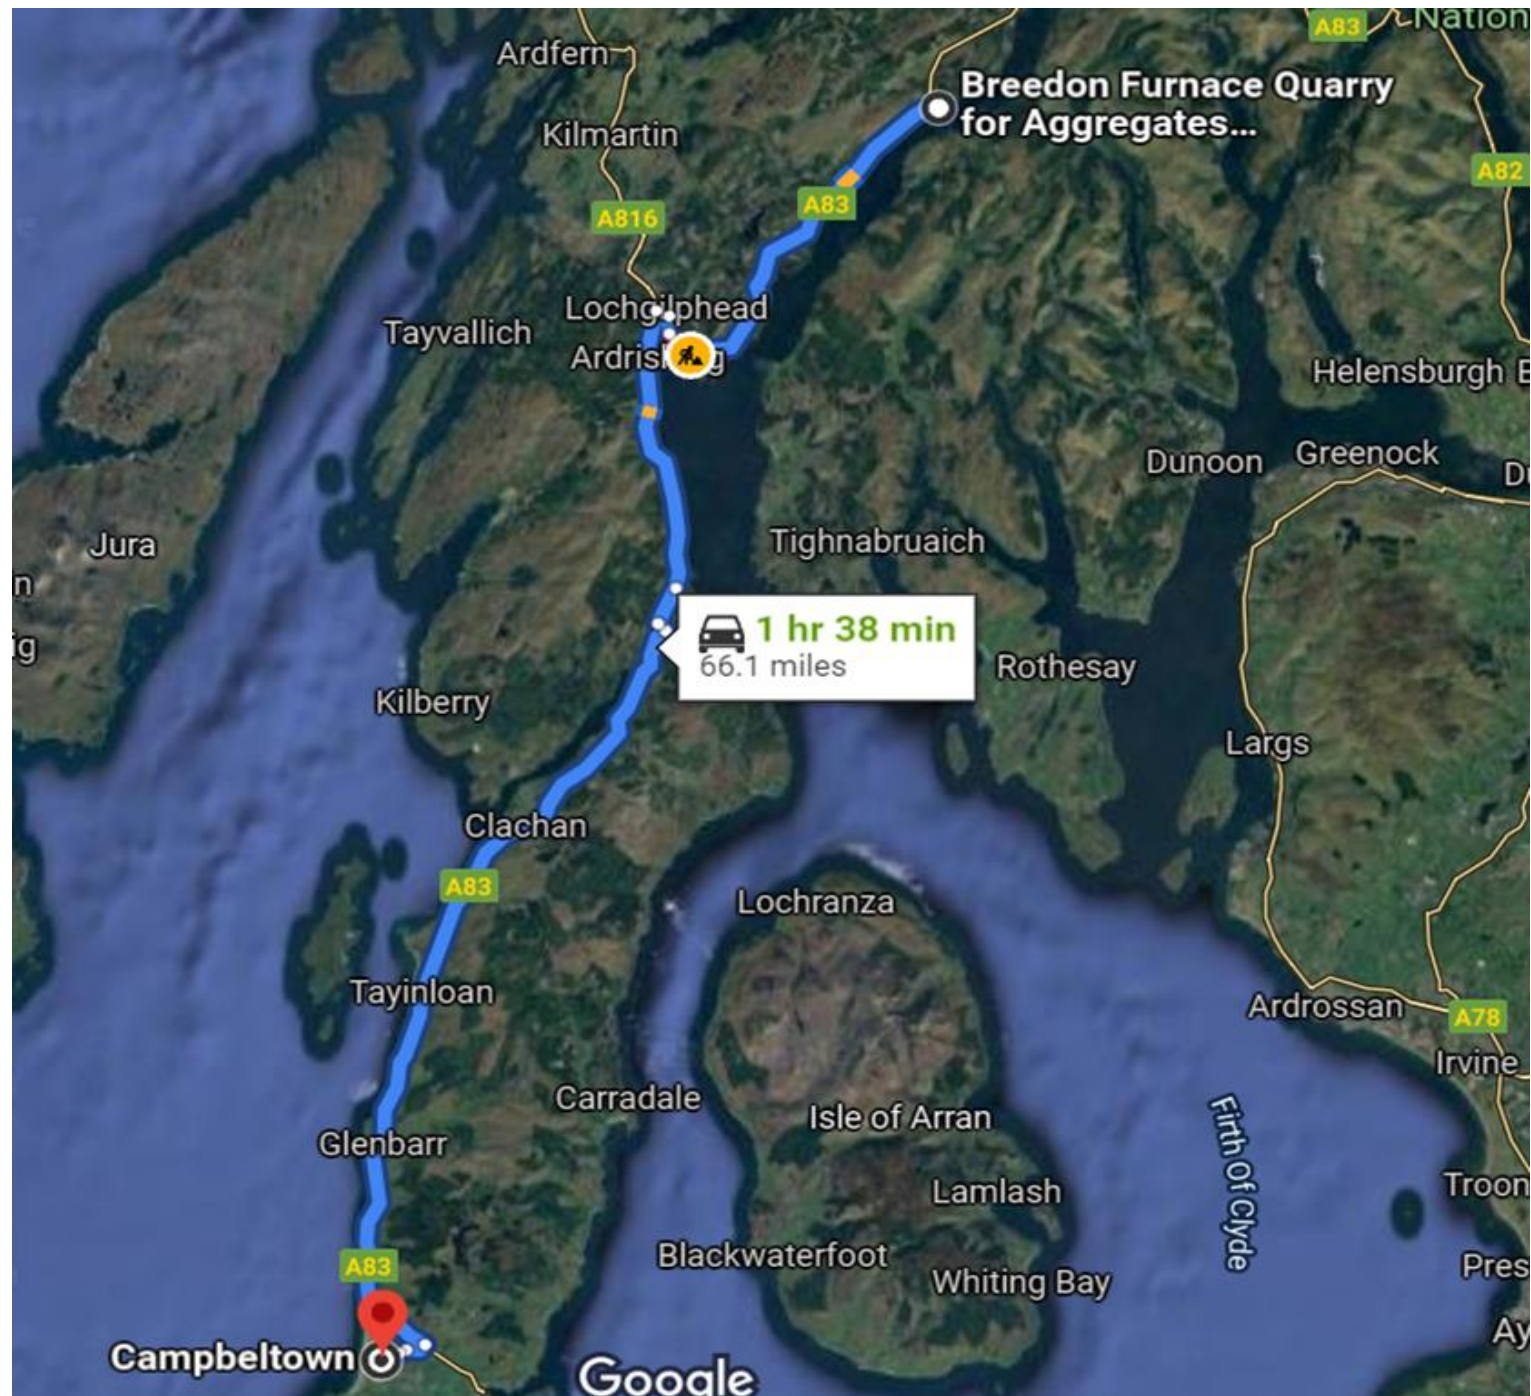

# 3. Access Routes

## Campbeltown Airport Road

1. 3.5 miles
2. Under jurisdiction of Council Argyll and Bute

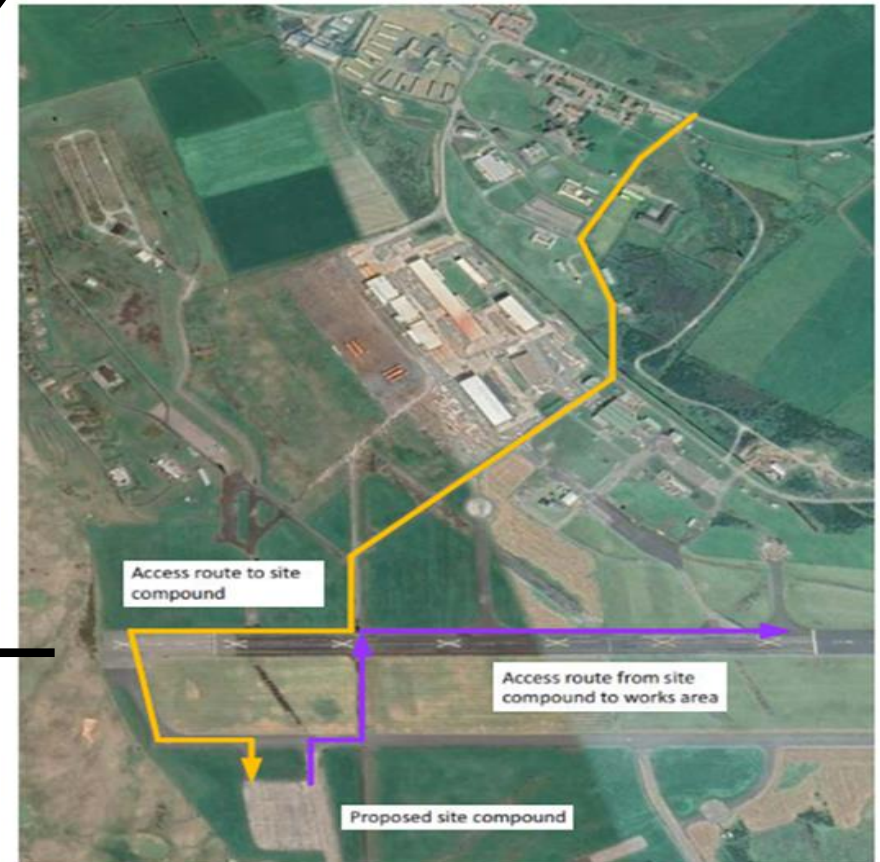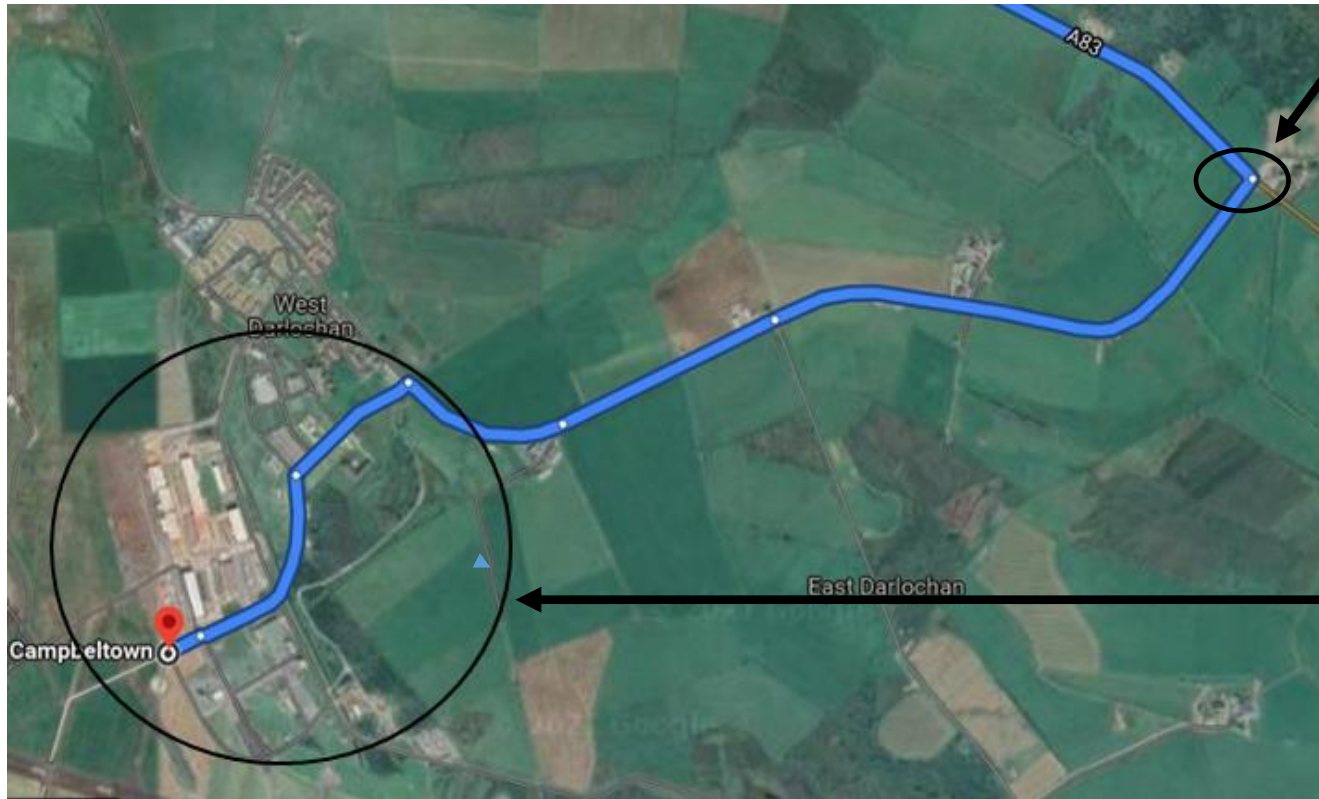



## 4. Next Steps

- Stakeholder to put in place processes and procedures.
- Weekly updates via HIAL website and emails.

# 5. Open Discussion
